



Corrective Action Response Pictures



Concrete washout has been emptied and adjacent spills along [redacted] and [redacted]. There are no stucco operations on-going at the site at this time. Stucco washouts will be placed on lots close to on-going work when stucco application recommences.

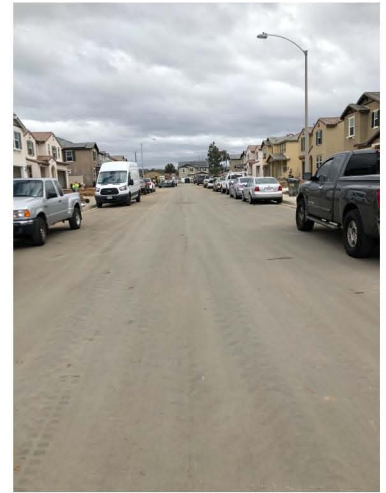

Tracking on driveways ramps and street has been removed, fiber roll installed to limit entry to lots and maintain sediment control prior to the forecasted rain event.

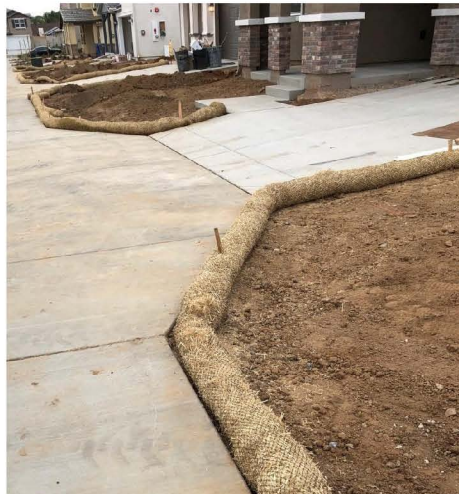

Tracking on driveway ramps and street has been removed, fiber roll installed to limit entry to lots and maintain sediment control prior to the forecasted rain event. Inlets were cleaned and maintained.
